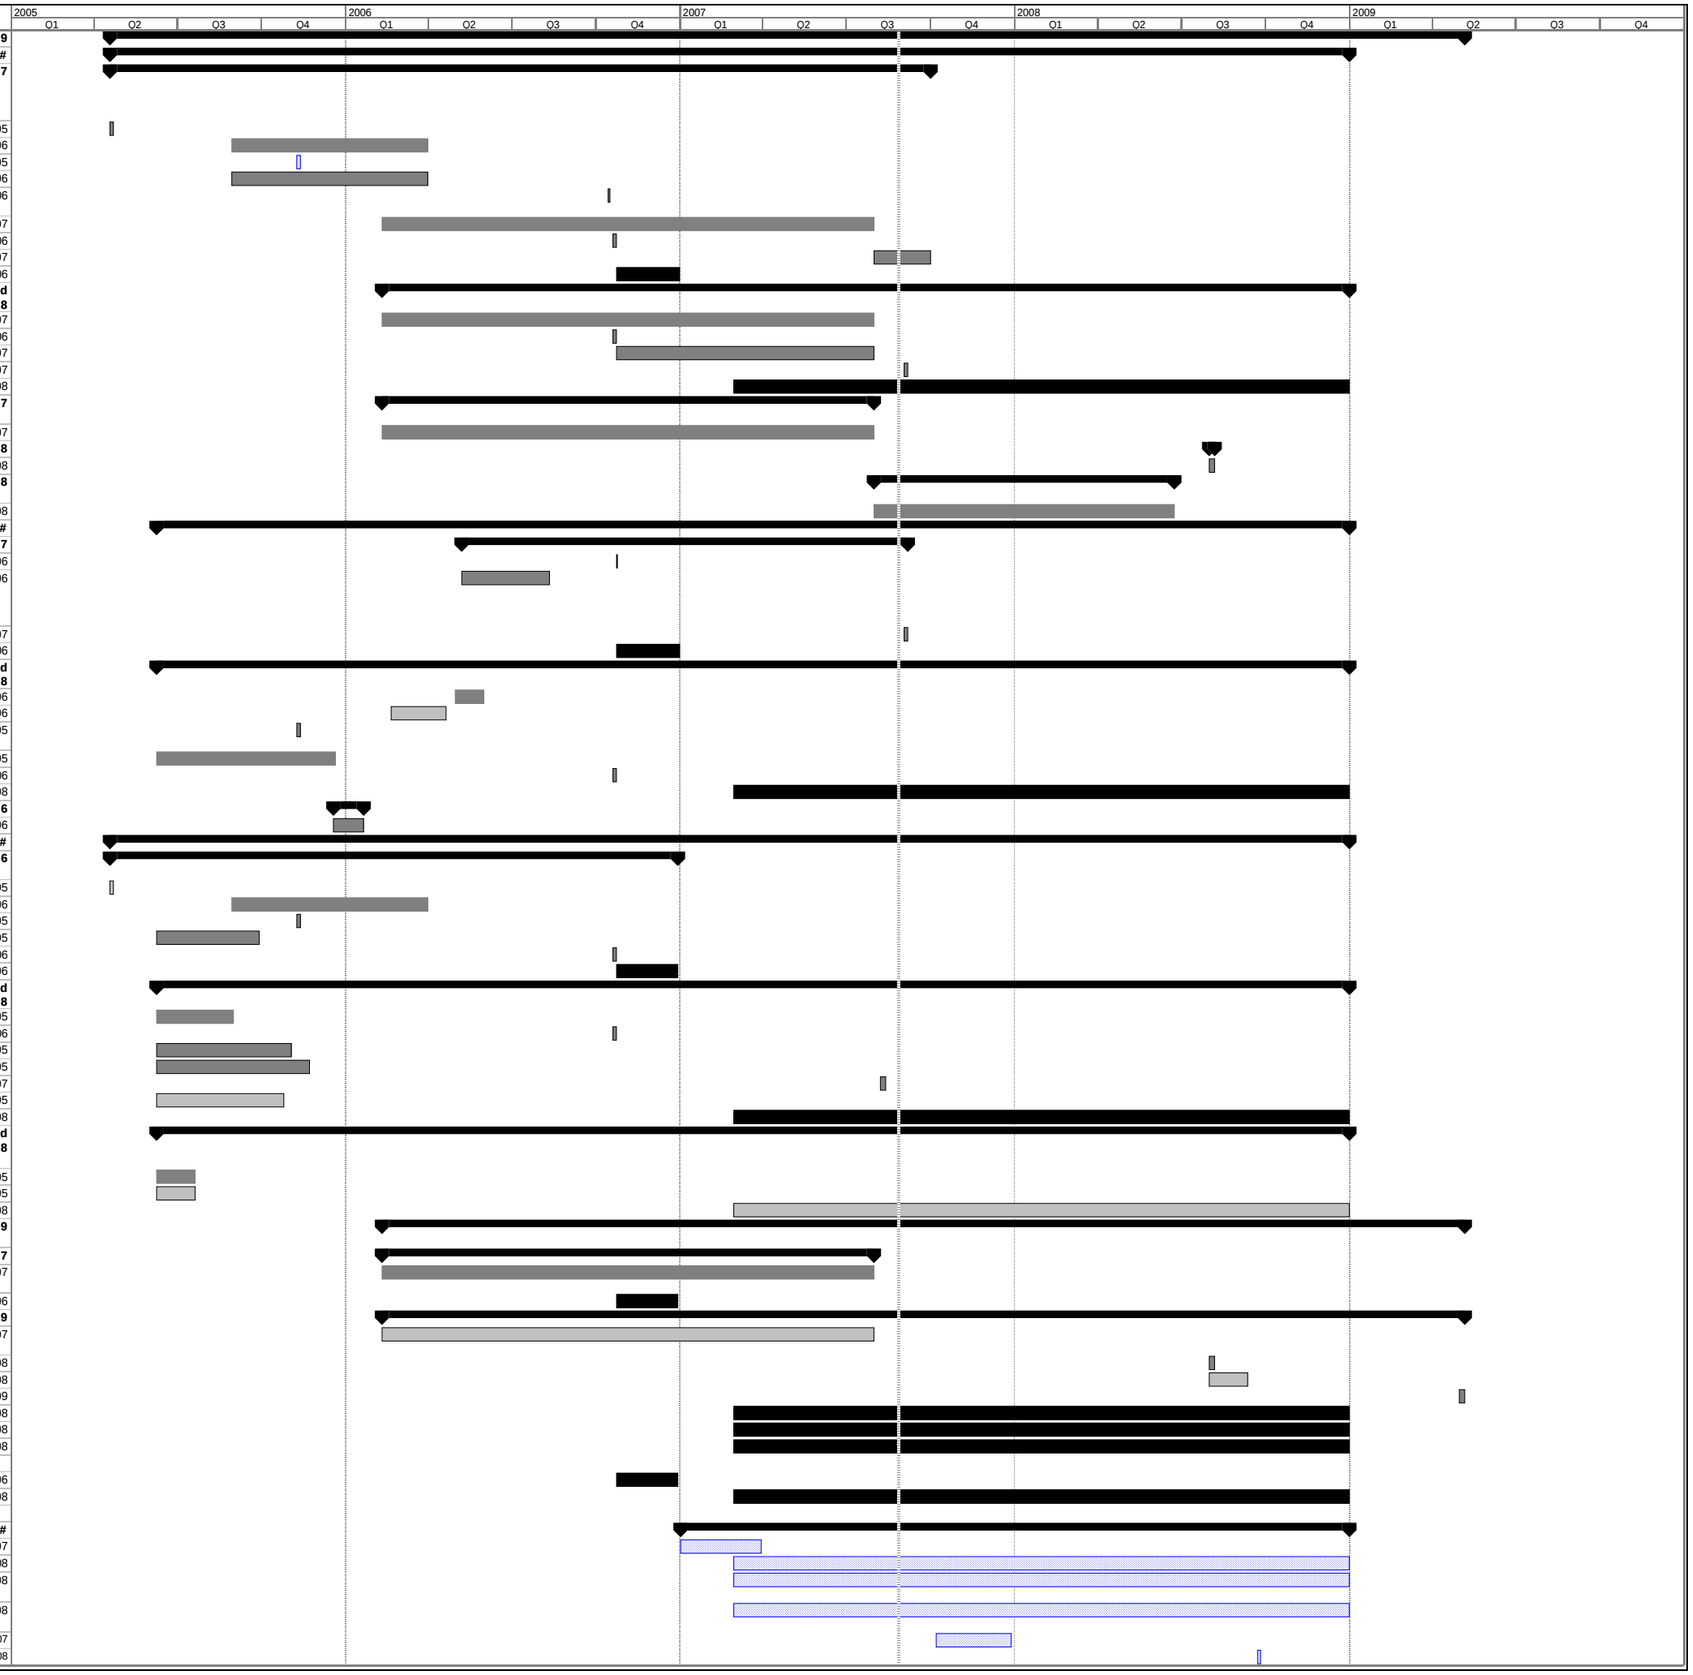ID	Task Name	Duration	Start	Finish
1	**OBJECTIVE II: BIODIVERSITY PROTECTION COMPONENT**	**1061 days?**	**Tue 4/19/05**	**Wed 5/6/09**
2	**IIA: HABITAT CONSERVATION AND VULNERABLE SPECIES**	**971 days?**	**Tue 4/19/05**	**#########**
3	**ACT 1: Review existing national practices of coastal habitat use, conservation, restoration, status of vulnerable species and trophic linkages (including keystone species), and analyse and prioritise gaps of regional importance; Identify capacity gaps…**	**644 days?**	**Tue 4/19/05**	**Mon 10/1/07**
4	WG Meeting 1 (Qingdao)	4 days	Tue 4/19/05	Fri 4/22/05
5	Contract to relevant national institution(s) (Contract C1)	155 days	Tue 8/30/05	Fri 3/31/06
6	WG Meeting 2	4 days	Wed 11/9/05	Sat 11/12/05
7	Finalise national outputs and synthesis	155 days	Tue 8/30/05	Fri 3/31/06
8	Consider cross- component meeting with other WGs to discuss trophic linkage outcomes relevant to other WGs	2 days?	Sun 10/15/06	Mon 10/16/06
9	Prepare a regional synthesis (consultant C2)	386 days	Fri 2/10/06	Tue 7/31/07
10	Present outcomes of national assessment in WG Meeting 3	2 days	Fri 10/20/06	Mon 10/23/06
11	Publish the outcomes (printing)	44 days?	Wed 8/1/07	Mon 10/1/07
12	Inputs to final TDA	49 days	Tue 10/24/06	Sun 12/31/06
13	**ACT 2: Develop regionally coordinated strategies of conservation and restoration of habitats and for protection of vulnerable species**	**757 days?**	**Fri 2/10/06**	**Wed 12/31/08**
14	Prepare draft regional strategy (Consultant C2)	386 days?	Fri 2/10/06	Tue 7/31/07
15	Discuss and modify the draft (WG Meeting 3)	2 days	Fri 10/20/06	Mon 10/23/06
16	Revise the draft accordingly (C2)	201 days	Tue 10/24/06	Tue 7/31/07
17	Finalise strategy (WG Meeting 4)	4 days	Mon 9/3/07	Thu 9/6/07
18	Inputs to regional SAP	480 days	Thu 3/1/07	Wed 12/31/08
19	**ACT 3: Implement regional strategy for conservation areas and the protection of vulnerable species**	**386 days**	**Fri 2/10/06**	**Tue 7/31/07**
20	Prepare draft implementation plan (consultant C2)	386 days	Fri 2/10/06	Tue 7/31/07
21	**ACT 4: Implement regional strategy for conservation areas**	**4 days**	**Fri 8/1/08**	**Wed 8/6/08**
22	Adopt implementation plan (WG Meeting 5)	4 days	Fri 8/1/08	Wed 8/6/08
23	**ACT 5: Implentation of regionally coordinated strategies for protection of vulnerable species**	**234 days**	**Wed 8/1/07**	**Mon 6/23/08**
24	Implement the strategy (contract to national focal points C3)	234 days	Wed 8/1/07	Mon 6/23/08
25	**IIB: GENETIC DIVERSITY - low priority activity, no budget**	**934 days**	**Thu 6/9/05**	**#########**
26	**ACT 1: Determine situations of genetic degradation of important bio-re**	**352 days**	**Mon 5/8/06**	**Thu 9/6/07**
27	Meeting to discuss Genetic Diversity at end of RWG3	1 day	Tue 10/24/06	Tue 10/24/06
28	Prepare draft of current status of genetic degradation of important bioresources, including a list of species and current activities which address 'genetic degredation' and identify and prioritise gaps [Communicate DIM management consultant]	70 days	Mon 5/8/06	Fri 8/11/06
29	Discuss and finalise current status (WG Meeting 4)	4 days	Mon 9/3/07	Thu 9/6/07
30	Inputs to TDA	49 days	Tue 10/24/06	Sun 12/31/06
31	**ACT 2: Develop regional concensus on the requirements for conservation of genetic diversity**	**934 days**	**Thu 6/9/05**	**Wed 12/31/08**
32	Prepare draft list on conservation of genetic diversity (consultants)	23 days	Mon 5/1/06	Wed 5/31/06
33	Training course on genetic techniques [delete this]	44 days	Mon 2/20/06	Thu 4/20/06
34	Agree list on genes (WG Meeting 2 delete) (during addition working group meeting)	4 days	Wed 11/9/05	Sat 11/12/05
35	Prepare a plan for the conservation (consultant)	140 days	Thu 6/9/05	Tue 12/20/05
36	Finalise the plan (WG Meeting 3)	2 days	Fri 10/20/06	Mon 10/23/06
37	Input to SAP	480 days	Thu 3/1/07	Wed 12/31/08
38	**ACT 3: Prepare recommendations for conservation measures**	**25 days**	**Mon 12/19/05**	**Fri 1/20/06**
39	The activities will be incorporated into activity 2	25 days	Mon 12/19/05	Fri 1/20/06
40	**IIC: EXOTIC (INTRODUCED) SPECIES**	**971 days?**	**Tue 4/19/05**	**#########**
41	**ACT 1: Document introduced exotic species and their pathways, assess impacts and risks**	**448 days**	**Tue 4/19/05**	**Fri 12/29/06**
42	WG Meeting 1	4 days	Tue 4/19/05	Fri 4/22/05
43	Contract to relevant national institution(s) (Contract C1)	155 days	Tue 8/30/05	Fri 3/31/06
44	Discuss and modify the draft (WG Meeting 2)	4 days	Wed 11/9/05	Sat 11/12/05
45	Revise the draft accordingly	80 days	Thu 6/9/05	Wed 9/28/05
46	Finalise the strategy (WG Meeting 3)	2 days	Fri 10/20/06	Mon 10/23/06
47	Inputs to TDA	49 days	Tue 10/24/06	Fri 12/29/06
48	**ACT 2: Develop proposals for regulation and control of exotic species - low priority, no budget**	**934 days?**	**Thu 6/9/05**	**Wed 12/31/08**
49	Prepare draft regulation to control exotic species (consultant)	60 days	Thu 6/9/05	Wed 8/31/05
50	Discuss the draft (WG Meeting 3)	2 days	Fri 10/20/06	Mon 10/23/06
51	Training course on the implementation of the regulation	105 days	Thu 6/9/05	Wed 11/2/05
52	Revise the draft accordingly	120 days?	Thu 6/9/05	Tue 11/22/05
53	Finalise strategy (WG Meeting 4)	4 days	Wed 8/8/07	Mon 8/13/07
54	Submit for approval of governments	99 days	Thu 6/9/05	Tue 10/25/05
55	Inputs to regional SAP	480 days	Thu 3/1/07	Wed 12/31/08
56	**ACT 3: Implement strategies for regulation and control of introduction of exotic species, including necessary legal, poliy and institutional reforms at national and regional levels - low priority, no budget**	**934 days?**	**Thu 6/9/05**	**Wed 12/31/08**
57	Upon approval, prepare an implementation plan (consultant)	30 days	Thu 6/9/05	Wed 7/20/05
58	Implement the regulation	30 days?	Thu 6/9/05	Wed 7/20/05
59	Inputs to regional SAP	480 days	Thu 3/1/07	Wed 12/31/08
60	**IID: SYNTHESIS OF REVIEWS AND DEVELOPMENT OF COORDINATED STRATEGIES**	**847 days**	**Fri 2/10/06**	**Wed 5/6/09**
61	**ACT 1: Synthsize reviews from IIA, B and C**	**386 days**	**Fri 2/10/06**	**Tue 7/31/07**
62	Consultant to synthesize output from activity HIGH of IIA, IIB, IIC (consultant C2)	386 days	Fri 2/10/06	Tue 7/31/07
63	Inputs to final TDA	49 days	Tue 10/24/06	Fri 12/29/06
64	**ACT 2: Develop coordinated strategy for biodiversity protection**	**847 days**	**Fri 2/10/06**	**Wed 5/6/09**
65	Synthesize 3 regional strategies and 3 implementation plans to prepare a coordinated regional SAP (consultant C2)	386 days	Fri 2/10/06	Tue 7/31/07
66	Discuss and prioritise actions in regional SAP (WG Meeting 5)	4 days	Fri 8/1/08	Wed 8/6/08
67	Revise the draft accordingly	30 days	Fri 8/1/08	Thu 9/11/08
68	Finalize strategy (WG Meeting 6?)	4 days	Fri 5/1/09	Wed 5/6/09
69	Inputs to regional SAP	480 days	Thu 3/1/07	Wed 12/31/08
70	Accept the Regional SAP	480 days	Thu 3/1/07	Wed 12/31/08
71	Submit for approval of governments	480 days	Thu 3/1/07	Wed 12/31/08
72				
73	**TDA COMPLETE**	49 days	Tue 10/24/06	Fri 12/29/06
74	**SAP COMPLETE**	480 days	Thu 3/1/07	Wed 12/31/08
75				
76	**Proposed New Activities**	**522 days?**	**Tue 1/2/07**	**#########**
77	Regional expert's consultation on developing regional biodiversity targets (S/	64 days	Tue 1/2/07	Fri 3/30/07
78	Development of robust criteria to identify critical habitats (WWF)	480 days	Thu 3/1/07	Wed 12/31/08
79	Development of regional agreements to delineate conservation areas and protection of vulnerable species (Coastal survey)	480 days	Thu 3/1/07	Wed 12/31/08
80	Identification of regional actions to mitigate threats from possible introduction of exotic species (SAP)	480 days?	Thu 3/1/07	Wed 12/31/08
81	Biodiversity advisor	60 days?	Mon 10/8/07	Fri 12/28/07
82	5th RWG-B	3 days?	Tue 9/23/08	Thu 9/25/08
